

Front of House Project Summary rev 2_19 Aug 2024

The Airport Development Group commenced with the Front of House construction works on 15 August 2024.


The high-level scope of the works can be summarised as follows.

- Demolish the current canopy paved area between lanes.
- All works associated with the relocation of the fire infrastructure / booster.
- Installation of PVC shade sails in front of the terminal building.
- Removable bollards to be installed at the eastern and western end in the two traffic lanes closest to be terminal building. These will used as a dedicated emergency vehicle access path.
- Landscaping rocks to be installed between PVC sail columns to serves as anti-terrorism measure.
- Minor landscaping to tie in with existing landscaping at Eastern end and curbing to finish off previous eastern approach road re-alignment work.


The intended work will take place right in front of the terminal building and it is foreseen that taxi operators and private hire / limousine services will be impacted by the execution of the project as well as the general traveling public.

The information provided below regarding the impact on taxis are preliminary and are subject to changes as the project progresses and more information becomes available, or construction challenges are experienced.

TGS 1 - During the first stage of the project which will involve the demotion of the current canopy structure, the taxi drop-off lane will be closed, and taxis are requested to drop passengers off via the 2-minute kiss and go lane, the taxi pick up lane will remain operational. *Estimated dates for implementation – 12 Aug 2024 to 22 Aug 2024*

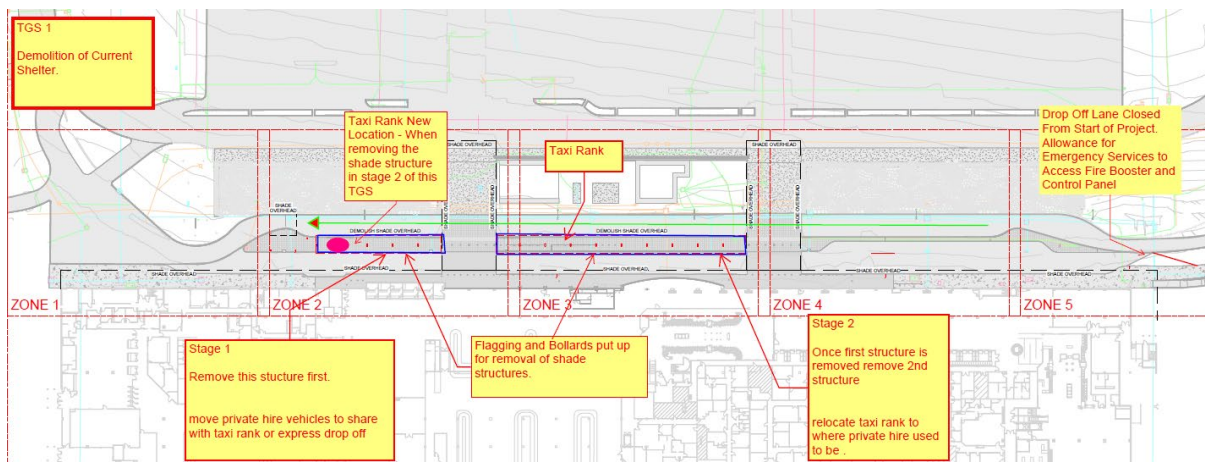

TGS 2- This stage of the project will involve the construction of the new fire equipment enclosure and trenching across the lanes closest to the terminal building to relay piping. The same will be in place in that the taxi drop-off lane will be closed, and taxis are requested to drop passengers off via the 2-minute kiss and go lane. The taxi pickup lane will remain operational. *Estimated Dates for Implementation 22 August to 6 September 2024*

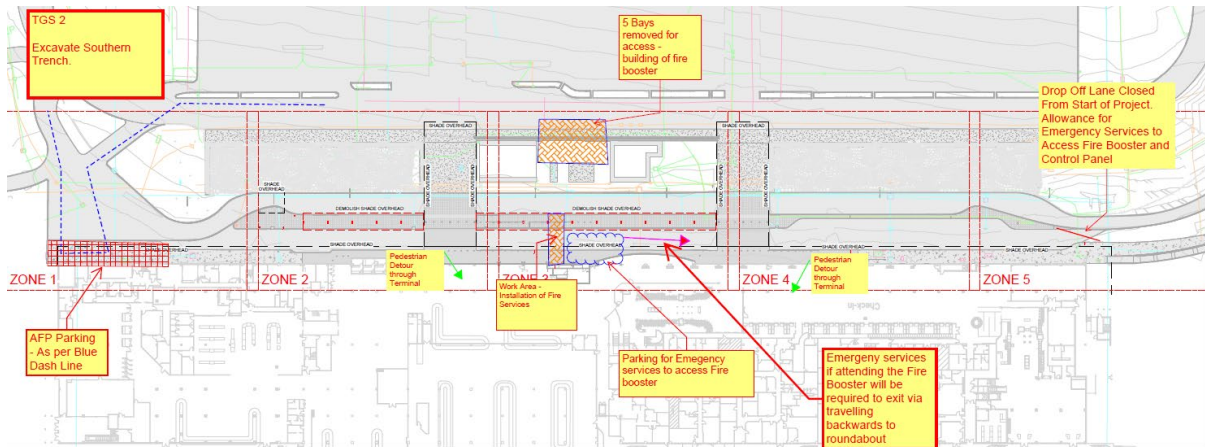

TGS 3 – During this stage taxis will continue to use the two-minute kiss and go lane for drop-off, but the lane closes to the terminal will become the pickup lane for a duration of approximately two weeks.

Following the completion of these works, there will be 10 weeks wait period before the steel structure supporting the sails and the PVC sails will be installed. More details regarding the installation of the steel structure and the impact on traffic will follow in due course. *Estimated Dates for Implementation 9 September to 27 September 2024*

